

DCBL/BGM/EC/COMP/H2/YKLM/2026/15

Date: 23.05.2026

To,

The Regional Director
Ministry of Environment, Forest & Climate Change
Regional Office (South Zone),
Kendriya Sadan, 4th Floor,
E & F wing, 17th Main Road,
II Block, Koramangala,
Bengaluru – 560034.

Dear Sir,

Sub: Submission of Half Year EC Compliance Report of M/s Dalmia Cement Bharat Limited, (Yadwad and Kunnal Limestone Mine) for the period Oct-2025 to March- 2026.

Ref: F.No.J-11015/36/2009 - IA II (M) Dated. 13th March 2015.

Dear Sir,

With Reference to the above, we are here with attached Half Year Environment Clearance compliance reports of M/s. Dalmia Cement (Bharat) Limited (Yadwad and Kunnal Limestone Mine), Yadwad villages, Mudalagi Taluk, Belgaum district, Karnataka, for the period of **Oct 2025 to March 2026**.

Kindly request to acknowledge the same.

Yours faithfully

For M/s. Dalmia Cement (Bharat) Limited, Belagavi


Authorised Signatory

- Cc:** 1. The Environmental Officer, Karnataka State Pollution Control Board, Plot No.6816/1/P-5, 5th cross, Harinagar, Chikkodi-591201.
2. The Member Secretary, Karnataka State Pollution Control Board, Parisara Bhavana, 1st to 5th Floor, #49, Chruch street, Bengaluru-560001.
3. Regional Officer, Central Pollution Control Board, Nisarga Bhavan, Thimmaiah Road, 7th D Main Rd, Shivanagar, Bengaluru, Karnataka - 560079.

Your (Half Yearly Compliance Report) has been Submitted with following details

Proposal No	J-11015/36/2009-IA.II (M)
Compliance ID	1227646027
Compliance Number(For Tracking)	EC/M/COMPLIANCE/1227646027/2026
Reporting Year	2026
Reporting Period	01 Jun(01 Oct - 31 Mar)
Submission Date	23-05-2026
RO/SRO Name	Shri S Senthil Kumar
RO/SRO Email	jk083.ifs@nic.in
State	KARNATAKA
RO/SRO Office Address	Integrated Regional Offices, Bengaluru
Note:- SMS and E-Mail has been sent to Shri S Senthil Kumar, KARNATAKA with Notification to Project Proponent.	

Half Yearly Compliance Report 2026 01 Jun(01 Oct - 31 Mar)			
Acknowledgement			
Proposal Name		Yadwad Limestone Mines of M/s Dalmia Cement (Bharat) Limited, village Yadwad and Kunnal, Distt. Belgaum, Karnataka (1228.63 Ha) (4.3 MTPA) - Environment Clearance	
Name of Entity / Corporate Office		Dalmia Cement (Bharat) Limited	
Village(s)		KUNNAL	
District		BELAGAVI	
Proposal No.	J-11015/36/2009-IA.II (M)	Category	Non-Coal Mining
Plot / Survey / Khasra No.		Sub-District	Ramdurg
State	KARNATAKA	Entity's PAN	*****9414C
MoEF File No.	J-11015/36/2009-IA.II (M)	Entity name as per PAN	DALMIA CEMENT (BHARAT) LIMITED
Compliance Reporting Details			
Reporting Year	2026		
Remarks (if any)	Submission of Half Yearly Environment Clearance condition wise compliance report for the period of Oct-2025 to March-2026.		
Reporting Period	01 Jun(01 Oct - 31 Mar)		
Details of Production and Project Area			
Name of Entity / Corporate Office	Dalmia Cement (Bharat) Limited		
	Project Area as per EC Granted	Actual Project Area in Possession	
.Private	1223.78	526.10	
Revenue Land	0	0	
Forest	0	0	
Others	N/A	N/A	
Total	1223.78	526.1	
Others Area			
Sr. no	Other Name	Area Granted	Area Actual

Production Capacity						
Sr. no	Product Name	units	Valid Upto	Capacity	Production last year	Capacity as per CTO
1	Limestone	Million Tons per Annum (MTPA)	31/03/2026	4.3	2.39	4.3
Conditions						
Specific Conditions						
Sr.No.	Condition Type	Condition Details				
1	Statutory compliance	The EC valid only for 1223.78 ha of land out of 1228.63 ha, subject to final outcome in all the Writ Petitions in the Karnataka High Court.				
PPs Submission: Agreed to Comply Noted. Lease granted area is 1048.24 Ha. Final outcome of all the writ petitions from Karnataka high court is still awaited.						Date: 14/05/2026
2	WATER QUALITY MONITORING AND PRESERVATION	The mining operations shall be restricted to above ground water table, and it should not intersect the groundwater table.				
PPs Submission: Complied Present mining operation is well above the ground water table.						Date: 14/05/2026
3	LAND RECLAMATION	The PP to provide unhindered access to the other lease holder(s) and farmers to their land in the lease area.				
PPs Submission: Complied Access to farmers having land in lease area is provided.						Date: 14/05/2026
4	LAND RECLAMATION	The loose solids should be kept separately from flowing water and flow of effluents to nearby areas outside the leasehold shall be prevented. The paved drains along with arrangements for Over Burden Dumps and their drainage may be clearly depicted on a contoured map of the mining area.				
PPs Submission: Complied Overburden dump is being maintained separately and protected from soil erosion by garland drains and retaining wall. There is no flow of water / effluents outside from the lease area.						Date: 14/05/2026
5	WATER QUALITY MONITORING AND PRESERVATION	Dimension of the retaining wall at the toe of the OB dump(s) and the OB benches within the mine to check run-off and siltation should be based on the rain fall data.				
PPs Submission: Complied Retaining wall constructed as per the approved mining plan wherein the rain fall data is considered.						Date: 14/05/2026
6	WATER QUALITY MONITORING AND PRESERVATION	Regular monitoring of water quality upstream and downstream of perennial nallahs falling in the impact zone shall be carried out and record of monitoring data should be maintained and submitted to Ministry of Environment, Forest and Climate Change, its Regional Office, Bangalore, Central Groundwater Authority, Regional				

		Director, Central Ground Water Board, State Pollution Control Board and Central Pollution Control Board.
PPs Submission: Complied Ground water level and quality is being monitored regularly in both core zone and buffer zone of the mining lease area. There is no effect of ground water table and water quality with the present mining activity. The report on Ground water level and quality is enclosed.		Date: 14/05/2026
7	Statutory compliance	The project proponent shall obtain Consent to Establish and Consent to Operate from the Karnataka State Pollution Control Board and effectively implement all the conditions stipulated therein.
PPs Submission: Complied Consent to Establishment vide order no. PCB/MIN/CFE/2015-16/296 and Combined Consent for Operation vide order number AW-326556 Dt.03.09.2021 obtained from Karnataka State Pollution Control Board and conditions are being effectively implemented.		Date: 14/05/2026
8	WASTE MANAGEMENT	The topsoil, if any shall temporarily be stored at earmarked site(s) only and it should not be kept unutilized for long. The topsoil shall be used for land reclamation and plantation
PPs Submission: Complied Topsoil is being stacked separately in the earmarked area as per mining plan. The same shall be utilized as per proposed reclamation plan and also being utilized for plantation.		Date: 14/05/2026
9	WASTE MANAGEMENT	Appropriate safeguard measures shall be taken to ensure stability and drainage of dump so that no solid waste/debris flows into the nallah.
PPs Submission: Complied Garland drain and retaining wall constructed around waste dump to prevent solid waste /debris flow. Photographs are attached herewith.		Date: 14/05/2026
10	WASTE MANAGEMENT	The over burden (OB) generated during the mining operation shall be stacked at earmarked dump site(s) only and it should not be kept active for a long period of time and their phase-wise stabilization shall be carried out. Proper terracing of OB dump(s) shall be carried out. The over burden dump(s) shall be scientifically Vegetated with suitable native species to prevent erosion and surface run off. In critical areas, use of geo textiles shall be undertaken for stabilization of the dumps. Monitoring and management of rehabilitated areas should continue until the vegetation becomes self-sustaining. Compliance status should be submitted to the Ministry of Environment, Forest and Climate Change and its Regional Office, Bangalore on six monthly basis.
PPs Submission: Complied Over burden is being stacked separately in the designated area and stabilization of the same shall be taken up as per the approved mining plan. Details of OB generated is attached.		Date: 14/05/2026
11	WASTE MANAGEMENT	To avoid adverse impact of mining operations on habitations/villages, the Project shall comply with conditions provided in OM no. Z-11013/57/2014- IA. II (M) dated 29.10.2014 on Impact of mining activities on Habitations-Issues related to the mining Projects wherein Habitations and villages are the part of mine lease areas or Habitations and villages are surrounded by the mine lease area.
PPs Submission: Complied There are no habitations/ village near to the present mine work and hence there is no adverse impact		Date:

on habitations/ villages due to mining operation. However, conditions are being complied.		14/05/2026
12	WATER QUALITY MONITORING AND PRESERVATION	Catch drains and siltation ponds of appropriate size shall be constructed for the working pit, temporary OB and mineral dumps to arrest flow of silt and sediment directly into the adjoining River and other water bodies. The water so collected should be utilized for watering the mine area, roads, green belt development etc. The drains should be regularly desilted particularly after the monsoon and maintained properly.
PPs Submission: Complied Catch drains are connected to siltation pond at working pit. Water is being utilized for dust suppression on haul roads and green belt development. No water is allowed to flow outside the lease area to river and other water bodies. Photographs of drains and siltation pond is enclosed.		Date: 14/05/2026
13	AIR QUALITY MONITORING AND PRESERVATION	Effective safeguard measures, such as regular water sprinkling shall be carried out in critical areas prone to air pollution and having high levels of particulate matter such as around crushing and screening plant, loading and unloading point and all transfer points. Extensive water sprinkling shall be carried out on haul roads. It should be ensured that the Ambient Air Quality parameters conform to the norms prescribed by the Central Pollution Control Board in this regard.
PPs Submission: Complied Water sprinklers have been installed all along the main haul road which are prone to dust emissions and water tanker of 10 KL capacity has been dedicated for suppressing fugitive dust emissions at source points. Ambient air quality is continuously monitored and maintained as per CPCB norms. Photographs of water sprinkling system for haul road and ambient air quality data are enclosed.		Date: 14/05/2026
14	WATER QUALITY MONITORING AND PRESERVATION	Suitable rainwater harvesting measures on long term basis shall be planned and implemented in consultation with the Regional Director, Central Ground Water Board.
PPs Submission: Complied Rain water harvesting with catch drains developed in strategic location inside the mines to collect all the possible water during monsoon.		Date: 14/05/2026
15	AIR QUALITY MONITORING AND PRESERVATION	Controlled blasting shall be practiced. The mitigative measures for control of ground vibrations and to arrest fly rocks and boulders should be implemented.
PPs Submission: Complied State of art (NONEL) technology being practiced for Controlling ground vibrations and to arrest fly rocks and boulders and the vibration level of each blast is being monitored and recorded. A Sample of ground vibration monitoring report is attached.		Date: 14/05/2026
16	WATER QUALITY MONITORING AND PRESERVATION	The project authority should implement suitable conservation measures to augment ground water resources in the area in consultation with the Regional Director, Central Ground Water Board.
PPs Submission: Complied Rain water harvesting pond in mine shall act as natural recharge point for enhancing the ground water table. In addition to this we have constructed rain water harvesting pond with catch drains to collect all the surface runoff during monsoon and to conserve the water. Photographs of rain water harvesting pond are attached.		Date: 14/05/2026
17	WATER QUALITY	The project proponent shall ensure that no natural watercourse

	MONITORING AND PRESERVATION	and/or water resources shall be obstructed due to any mining operations. Adequate measures shall be taken for conservation and protection of the 1st and 2nd order streams, emanating or passing through the mine lease during the course of mining operation.
PPs Submission: Complied There is no water course inside the lease block boundaries.		Date: 14/05/2026
18	AIR QUALITY MONITORING AND PRESERVATION	Mineral handling area shall be provided with the adequate number of high efficiency dust extraction system. Loading and unloading areas including all the transfer points should also have efficient dust control arrangements. These should be properly maintained and operated.
PPs Submission: Complied Fugitive dust generation is being controlled in mineral handling areas by dedicated water tankers whereas, the lime stone crusher is equipped with bag filter and transfer towers are provided with water sprinkling system. The report on fugitive emission at mines is enclosed.		Date: 14/05/2026
19	MISCELLANEOUS	Provision shall be made for the housing of construction labor within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, mobile STP, safe drinking water, medical health care, creche etc. The housing may be in the form of temporary structures to be removed after the completion of the project.
PPs Submission: Complied Being mining operation no major construction activities are involved. All the workmen residing in village Yadwad, Mudhol and also being complied.		Date: 14/05/2026
20	WATER QUALITY MONITORING AND PRESERVATION	Sewage treatment plant shall be installed for the colony. ETP shall also be provided for the workshop and wastewater generated during the mining operation.
PPs Submission: Complied Sewage Treatment Plant of capacity 215 KL/day is installed at colony. Workshop water is treated in Effluent Treatment Plant.		Date: 14/05/2026
21	GREENBELT	The project proponent should take all precautionary measures during mining operation for conservation and protection of endangered flora as well as endangered fauna in the study area. Action plan for conservation of flora and fauna shall be prepared and implemented in consultation with the State Forest and Wildlife Department. Necessary allocation of funds for implementation of the conservation plan shall be made and the funds so allocated shall be included in the project cost. Copy of action plan may be submitted to the Ministry and its Regional Office at Bangalore within 3 months.
PPs Submission: Complied No endangered flora and fauna was identified in the study area of 10 km from the project site. Hence it doesnot require any action. Copies of the Baseline study conducted for preparation of EIA EMP are submitted to Ministry and its regional Office.		Date: 14/05/2026
22	AIR QUALITY MONITORING AND PRESERVATION	Regular monitoring of free silica in the dust will be carried out and records maintained. It shall be ensured that the levels of silica do not exceed the prescribed limit. The workers will be provided with personal protective measures to guard against in hailing silica dust.
PPs Submission: Complied Regular monitoring of free silica in the dust is being monitored. The level of silica is under		Date: 14/05/2026

prescribed limit. Report is attached.		
23	MINING PLAN	A Final Mine Closure Plan along with details of Corpus Fund should be submitted to the Ministry of Environment, Forest and Climate Change 5 years in advance of final mine closure for approval.
PPs Submission: Agreed to Comply Noted and shall be complied		Date: 14/05/2026
24	WATER QUALITY MONITORING AND PRESERVATION	Appropriate measures shall be taken for treatment of the upper catchment of the mine lease area
PPs Submission: Being Complied Rain water harvesting pond of 40000 m3 along with channels is developed in a strategic location to collect the maximum rain water during monsoon.		Date: 14/05/2026
25	WATER QUALITY MONITORING AND PRESERVATION	Regular monitoring of ground water level and quality shall be carried out in and around the mine lease by establishing a network of existing wells and installing new piezometers during the mining operation. The periodic monitoring (at least four times in a year- pre-monsoon (April-May), monsoon (August), post-monsoon (November) and winter (January); once in each season) shall be carried out in consultation with the State Ground Water Board/Central Ground Water Authority and the data thus collected may be sent regularly to the Ministry of Environment, Forest and Climate Change and its Regional Office Bangalore, the Central Ground Water Authority and the Regional Director, Central Ground Water Board. If at any stage, it is observed that the groundwater table is getting depleted due to the mining activity, necessary corrective measures shall be carried out.
PPs Submission: Being Complied Ground water level and quality is being monitored regularly in both core zone and buffer zone of the mining lease area. There is no effect of ground water table and water quality with the present mining activity. The report on Ground water level and quality is enclosed		Date: 14/05/2026
26	WATER QUALITY MONITORING AND PRESERVATION	The project proponent shall obtain necessary prior permission of the competent authorities for drawl of requisite quantity of water, required for the project.
PPs Submission: Being Complied We are utilizing rain water from Rain water harvesting to meet the requirement for mines.		Date: 14/05/2026
27	AIR QUALITY MONITORING AND PRESERVATION	The critical parameters such as RSPM (Particulate matter with size less than 10 micron i.e., PM10) and NOx in the ambient air within the impact zone, peak particle velocity at 300m distance or within the nearest habitation, whichever is closer shall be monitored periodically. Further, quality of discharged water shall also be monitored (TDS, DO, PH and Total Suspended Solids (TSS)). The monitored data shall be uploaded on the website of the company as well as displayed on a display board at the project site at a suitable location near the main gate of the Company in public domain. The Circular No. J-20012/1/2006-11A.11(M) dated 27.05.2009 issued by Ministry of Environment, Forest and Climate Change, which is available on the website of the Ministry www.envfor.nic.in shall also be referred in this regard for its compliance.

PPs Submission: Being Complied Ambient Air quality is being monitored periodically in both core and buffer zone areas. Peak particle velocity is monitored at 300 m distance. The discharged water quality is also monitored on regular basis.		Date: 14/05/2026
28	AIR QUALITY MONITORING AND PRESERVATION	Vehicular emissions shall be kept under control and regularly monitored. Measures shall be taken for maintenance of vehicles used in mining operations and in transportation of mineral. The mineral transportation shall be carried out through the covered trucks only and the vehicles carrying the mineral shall not be overloaded.
PPs Submission: Being Complied Emission from Vehicle are being maintained as per norms. All preventive maintenance jobs are carried out as per schedule. No dumper is overloaded with mineral (Lime stone). Roads are maintained and kept wet to avoid/ reduce fugitive emissions.		Date: 14/05/2026
29	Statutory compliance	Pre-placement medical examination and periodical medical examination of the workers engaged in the project shall be carried out and records maintained. For the purpose, schedule of health examination of the workers should be drawn and followed accordingly.
PPs Submission: Being Complied Pre-placement medical examination conducted for the workers employed and same will be done for future employment. Schedule for periodical health examination is prepared and being implemented.		Date: 14/05/2026
30	WATER QUALITY MONITORING AND PRESERVATION	Appropriate mitigative measures should be taken to prevent pollution of nearby River in consultation with the State Pollution Control Board.
PPs Submission: Being Complied All preventive measures taken and no water from mine lease flow in to the river.		Date: 14/05/2026
31	AIR QUALITY MONITORING AND PRESERVATION	Drills shall either be operated with dust extractors or equipped with water injection system
PPs Submission: Being Complied We are using state of art drill machine which is equipped with in built dust collectors and equipped with water injection system for wet drilling.		Date: 14/05/2026
32	PUBLIC HEARING	The project proponent shall undertake all the commitments made during the public hearing and effectively address the concerns raised by the locals in the public hearing as well as during consideration of the project, while implementing the project.
PPs Submission: Being Complied Commitments towards welfare of the local community are being carried out by adopting villages and providing ODF facility and many other CSR activities like clean water, water reservoir, check dam and drip irrigation etc.		Date: 14/05/2026
33	GREENBELT	Plantation shall be raised in a specified area including a 7.5 m wide green belt in the safety zone around the mining lease, OB dump(s), along the roads, etc. by planting the native species in consultation with the local DFO/Agriculture Department. In addition, plantation shall also be raised in the backfilled and reclaimed area and around water body. The density of the trees should be around 1500 plants per ha.

PPs Submission: Agreed to Comply Plantation proposed in phased manner covering safety zone of 7.5 m and other proved non-mineralised area. Plantation is being carried as per proposal with local species suggested by forest department. Nurturing and watering of the plantation made is being carried out on continuous basis to sustain the survival rate of the green belt and photographs of plantation are enclosed.		Date: 14/05/2026
General Conditions		
Sr.No.	Condition Type	Condition Details
1	WATER QUALITY MONITORING AND PRESERVATION	Industrial wastewater (workshop and wastewater from the mine) should be properly collected, treated so as to conform to the standards prescribed under GSR 422 (E) dated 19th May 1993 and 315 December 1993 or as amended from time to time. Oil and grease trap should be installed before discharge of workshop effluents
PPs Submission: Agreed to Comply No industrial water is being generated at present working. However, workshop water is treated in ETP and treated water meets GSR 422 E standard. Report on treated water is enclosed		Date: 14/05/2026
2	AIR QUALITY MONITORING AND PRESERVATION	Data on ambient air quality RSPM (Particulate matter with size less than 10 micron i.e., PM10) and NOx should be regularly submitted to the Ministry of Environment, Forest and Climate Change including its Regional office located at Bangalore and the State Pollution Control Board / Central Pollution Control Board once in six months.
PPs Submission: Being Complied Monitoring data of Ambient Air Quality and RSPM are submitted to the board on six-month basis.		Date: 14/05/2026
3	AIR QUALITY MONITORING AND PRESERVATION	Fugitive dust emissions from all the sources should be controlled regularly. Water spraying arrangement on haul roads, loading and unloading and at transfer points should be provided and properly maintained.
PPs Submission: Being Complied Water sprinkling is being carried out with two nos. dedicated 10 KL water tanker on all the source of emissions. Drilling is done by adopting wet drilling technology, water sprinkling system is installed for haul road and unloading point as well as transfer points.		Date: 14/05/2026
4	Statutory compliance	A separate environmental management cell with suitable qualified personnel should be set-up under the control of a Senior Executive, who will report directly to the Head of the Organization.
PPs Submission: Being Complied Environment Management cell established with qualified Environmental Officer.		Date: 14/05/2026
5	AIR QUALITY MONITORING AND PRESERVATION	Four ambient air quality-monitoring stations should be established in the core zone as well as in the buffer zone for RSPM (Particulate matter with size less than 10micron i.e., PM10) and NOx monitoring. Location of the stations should be decided based on the meteorological data, topographical features and environmentally and ecologically sensitive targets and frequency of monitoring should be undertaken in consultation with the State Pollution Control Board
PPs Submission: Being Complied Regular monitoring is being carried out at 4 core zone areas as well as 4 buffer zone areas. Report on		Date: 15/05/2026

Ambient Air Quality is enclosed		
6	Statutory compliance	The project proponent shall submit six monthly reports on the status of compliance of the stipulated Environmental Clearance conditions including results of monitored data (both in hard copies as well as by e-mail) to the Ministry of Environment, Forest and Climate Change, its Regional Office Bangalore, the respective Zonal Office of Central Pollution Control Board the State Pollution Control Board. The proponent shall upload the status of compliance of the Environmental Clearance conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of the Ministry of Environment, Forest and Climate Change, Bangalore, the respective Zonal Office of Central Pollution Control Board and the State Pollution Control Board
PPs Submission: Being Complied Being Complied with six monthly reports on EC conditions to Regional office - MOEFCC and also uploaded to our company web site		Date: 15/05/2026
7	WASTE MANAGEMENT	No change in the calendar plan including excavation, quantum of mineral limestone and waste should be made.
PPs Submission: Being Complied Mining and excavation are as per approved Mine plan.		Date: 15/05/2026
8	MINING PLAN	The project authorities should inform the Regional Office located at Bangalore regarding date of financial closures and final approval of the project by the concerned authorities and the date of start of land development work
PPs Submission: Agreed to Comply Noted		Date: 15/05/2026
9	Noise Monitoring & Prevention	Measures should be taken for control of noise levels below 85dBA in the work environment. Workers engaged in operations of HEMM, etc. should be provided with ear plugs / muffs.
PPs Submission: Agreed to Comply All workmen employed were provided with PPE's including ear plugs and muffs. Noise level is also being monitored on regular interval. Report on Noise levels is enclosed		Date: 15/05/2026
10	Statutory compliance	The State Pollution Control Board should display a copy of the clearance letter at the Regional office, District Industry Centre and the Collector's office/ Tehsildar's Office for 30 days.
PPs Submission: Agreed to Comply Its board jurisdictions.		Date: 15/05/2026
11	Human Health Environment	Personnel working in dusty areas should wear protective respiratory devices and they should also be provided with adequate training and information on safety and health aspects. Occupational health surveillance program of the workers should be undertaken periodically to observe any contractions due to exposure to dust and take corrective measures, if needed.
PPs Submission: Being Complied		Date:

Use of PPE is mandatory in mine working Adequate training is being provided on safety and health at our mine vocational training centre. Occupational health surveillance programs are conducted periodically.		15/05/2026
12	Statutory compliance	The Regional Office of this Ministry located at Bangalore shall monitor compliance of the stipulated conditions. The project authorities should extend full cooperation to the officer (s) of the Regional Office by furnishing the requisite data / information / monitoring reports.
PPs Submission: Agreed to Comply Compliance data and reports shall be made available to the Regional office as per the requirement.		Date: 15/05/2026
13	Statutory compliance	The funds earmarked for environmental protection measures should be kept in separate account and should not be diverted for other purpose. Year wise expenditure should be reported to the Ministry of Environment, Forest and Climate Change and its Regional Office located at Bangalore.
PPs Submission: Being Complied Funds separately allocated and maintained for Environment protection measures. Annual expenditure shall be provided in Environmental Statement.		Date: 15/05/2026
14	Statutory compliance	A copy of the clearance letter shall be sent by the proponent to concern Panchayat, Zila Parishad/ Municipal Corporation, Urban Local Body and the Local NGO, if any, from whom suggestions/ representations, if any, were received while processing the proposal. The clearance letter shall also be put on the website of the Company by the proponent
PPs Submission: Complied Copy of the EC letter have sent to the concern local body.		Date: 15/05/2026
15	Statutory compliance	The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall be put on the website of the company along with the status of compliance of Environmental Clearance conditions and shall also be sent to the Regional Office of the Ministry of Environment, Forest and Climate Change, Bangalore by e-mail
PPs Submission: Being Complied Form - V is being submitted to the Board on time i.e, before 30st Sep.		Date: 15/05/2026
16	Statutory compliance	The project authorities should advertise at least in two local newspapers of the District or State widely circulated in which the project is located and one of which shall be in the vernacular language of the locality concerned, within 7 days of the issue of the clearance letter informing that the project has been accorded Environmental Clearance and a copy of the clearance letter is available with the State Pollution Control Board and also at web site of the Ministry of Environment, Forest and Climate Change at http://envfor.nic.in and a copy of the same should be forwarded to the Regional Office of this Ministry located at Bangalore.

PPs Submission: Complied Advertised in The New Indian Express and Udayavani (vernacular language) on 21st March 2015. A copy of the same forwarded to the regional office of this ministry located at Bangalore.		Date: 15/05/2026
Visit Remarks		
Last Site Visit Report Date:	N/A	
Additional Remarks:		
Note: This acknowledgement is as per the details submitted by project proponent. In no way is this document to be considered as conclusion on any action on the compliance of the project. This is strictly for the project proponent's reference purpose.		

GROUND WATER ANALYSIS REPORT

GROUND WATER ANALYSIS REPORT																
Sl No	Parameters	Location code	DCGW1	DCGW2	Nov-25				Mar-26				DCGW5	DCGW6	Permissible Limits IS:10500:2012	
					DCGW3	DCGW4	DCGW5	DCGW6	DCGW1	DCGW2	DCGW3	DCGW4				
		Unit														
1	pH	-	7.43	7.40	7.52	7.75	7.87	7.87	7.72	7.62	7.83	7.5	7.63	7.53	-	
2	Conductivity	µs/cms	1640	1400	1580	1600	1640	1900	1820	1610	1660	1740	1660	1940	-	
3	Total Dissolved Solids	mg/L	980	840	942	960	980	1140	1110	980	1010	1060	1010	1180	2000	
4	Turbidity	NTU	0.2	0.2	0.3	0.2	0.2	0.4	0.3	0.3	0.3	0.2	0.2	0.3	5	
5	Total Suspended Solids	mg/L	4.0	<1.0	<1.0	<1.0	<1.0	<1.0	Nil	<1.0	<1.0	<1.0	<1.0	<1.0	-	
6	Sulphate as SO4	mg/L	212.48	186.22	202	186.28	174.84	242.68	196.41	168.18	191	192.5	179.1	217.3	400	
7	Phosphorous as P	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	-	
8	Sodium as Na	mg/L	86.12	74.06	94.74	90.06	102.72	86.12	92.3	77.33	89.46	94.1	98.1	81.2	-	
9	Potassium as K	mg/L	4.28	6.08	6.88	0.00	0.00	0.00	5.17	6.74	7.17	0.00	0.00	0.00	-	
10	Calcium as Ca	mg/L	149.89	121.04	152.30	169.93	192.38	169.93	153.69	124.8	144.51	160.5	176.4	148.5	200	
11	Magnesium as Mg	mg/L	1.76	15.89	2.24	43.17	2.68	39.16	1.54	13.96	2.83	48.4	2.87	34.6	100	
12	Total Hardness as CaCO3	mg/L	382.0	368.0	390.0	468.0	492.00	586	390	370.0	373	582.17	453.0	513	600	
13	Chloride as Cl	mg/L	154.24	127.24	152.31	168.7	235.21	280.52	163.4	119.28	159.11	160.4	201.4	262.3	1000	
14	Fluoride as F	mg/L	0.46	0.62	0.48	0.36	0.38	0.42	0.57	0.59	0.63	0.41	0.44	0.38	1.5	
15	Nitrate Nitrogen as NO3	mg/L	12.58	10.54	12.56	14.02	7.66	10.18	13.66	11.18	12.88	15.6	6.18	0.92	NR	
16	Total Alkalinity as CaCO3	mg/L	420.00	462.0	440.0	420.0	388.0	460.0	482	454.1	396	382	342	428	600	
17	Acidity as CaCO3	mg/L	0.0	0.0	0.0	0.00	0.0	0.0	0.00	0.0	0.0	0.0	0.0	0.0	-	
18	Total Iron as Fe	mg/L	0.10	0.14	0.12	0.10	0.12	0.10	0.11	0.13	0.11	0.11	0.11	0.11	NR	
19	Nickel as Ni	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	0.02	
20	Manganese as Mn	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	0.3	
21	Copper as Cu	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	1.5	
22	Zinc as Zn	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	15	
23	Lead as Pb	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	0.01	
24	Silver as Ag	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	0.1	
25	Chromium as Cr	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	NR	
26	Mercury as Hg*	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	BDL	NR	
27	Colour	Hazen units	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	15	
28	Ambient Temperature	°C	25.2	25.4	25.0	25.2	25.4	25.2	25.7	25.4	25.6	25.7	25.1	25.8	-	
29	Dissolved Oxygen	mg/L	4.8	4.2	3.8	3.4	4.0	4.2	4.2	3.8	4.4	3.9	4.6	3.9	-	
30	Biochemical Oxygen Demand for 3 days at 27°C	mg/L	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	-	
31	Chemical Oxygen Demand	mg/L	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	-	
32	Oil & Grease	mg/L	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	-	
33	Total Coliform count*	MPN/ 100 ml	Absent	Absent	Absent	Absent	Absent	Absent	Absent	Absent	Absent	Absent	Absent	Absent	-	
34	Escherichia coli count*	MPN/ 100 ml	Absent	Absent	Absent	Absent	Absent	Absent	Absent	Absent	Absent	Absent	Absent	Absent	-	



DALMIA CEMENT (BHARAT) LIMITED

EC Half Yearly Compliance
Period: October 2025 to March 2026

GROUND WATER LEVEL MONITORING			
S.No	Location Name	Ground water level in meters from GL	
		Nov-25	Mar-26
1	Manami Village	11.13	12.83
2	Near Main Gate	12.60	14.37
3	Guest House	9.27	11.17
4	Near Mines Office	10.40	11.27

Garland Drains with siltation ponds



FY-25-26 Production/Waste/Top Soil Details

Month & Year	Limestone Tons	Waste/OB Tons	Top Soil Tons
October-2025	228837.9	33500	4725
November-2025	124849.32	78750	2655
December-2025	155234.84	49300	6525
January-2026	191861.16	22650	29340
February-2026	244351.36	10950	10575
March-2026	250582.06	20700	19440
Total	1195716.64	215850	73260

DALMIA CEMENT (BHARAT) LIMITED
EC Half Yearly Compliance
Period: October 2025 to March 2026
Ambient Air Quality Monitoring Report fy-25-26

Ambient Air Quality Monitoring Report fy-25-26																				
WA I. – West Side of Mines					SA II. – South Side of Mines					NA III. – North Side of Mines					EA IV. – East side of Mines					
Date	PM ₁₀ (µg/m3)	PM _{2.5} (µg/m3)	SO ₂ (µg/m3)	NO ₂ (µg/m3)	PM ₁₀ (µg/m3)	PM _{2.5} (µg/m3)	SO ₂ (µg/m3)	NO ₂ (µg/m3)	PM ₁₀ (µg/m3)	PM _{2.5} (µg/m3)	SO ₂ (µg/m3)	NO ₂ (µg/m3)	PM ₁₀ (µg/m3)	PM _{2.5} (µg/m3)	SO ₂ (µg/m3)	NO ₂ (µg/m3)	PM ₁₀ (µg/m3)	PM _{2.5} (µg/m3)	SO ₂ (µg/m3)	NO ₂ (µg/m3)
10.10.2025	39.82	11.2	13.31	16.5	33.45	9.53	9.36	10.53	41.08	9.37	9.99	12.1	31.58	8.04	8.56	12.06				
11.10.2025	50.29	17.78	10.7	13.32	49.26	6.2	8.78	9.29	51.2	12.59	11.74	13.1	46.01	13.68	9.55	11.78				
15.10.2025	51.81	10.81	14.79	16.82	45.91	9.06	10.14	10.75	69.39	11.79	9.2	11.83	53.17	9.9	11.07	13.07				
16.10.2025	55	14.28	11.23	14.32	42.95	13.53	8.83	9.4	43.62	16.04	12.14	14.51	49.26	10.08	8.28	12.72				
21.10.2025	46.92	13.38	10.31	13.07	44.26	7.19	7.3	10.04	50.98	13.79	10.92	13.24	47.61	15.98	10.57	12				
22.10.2025	49.6	12.5	8.02	11.01	47.24	9.81	7.72	9.2	58.92	14.33	8.36	10.91	52.94	10.56	9.13	14.07				
29.10.2025	46.43	12.47	12.81	15.27	33.04	7.52	6.81	9.87	51.57	11.98	9.56	11.52	50.36	9.58	8.32	13.7				
30.10.2025	50.89	8.94	10.89	13.86	45.8	7.87	9.38	11.94	57.07	13.41	10.41	11.89	45.0	11.97	9.11	13.45				
04.11.2025	67.08	16.62	7.63	8.82	48.61	15.69	7.14	8.99	77.08	19.44	7.26	8.48	59.25	18.79	7.52	9.76				
05.11.2025	66.24	22.34	10.42	11.14	59.79	14	8.71	9.03	64.92	25.63	9.55	10.95	68.69	16.28	9.43	10.09				
14.11.2025	60.76	25.36	9.92	12.43	51.89	15.43	6.89	7.69	70.28	18.94	8.8	11.24	70.54	18.6	9.17	11.18				
15.11.2025	55.05	18.57	12.35	12.77	43.49	17.71	7.91	8.56	62.85	21.86	10.98	12.25	56.19	14.94	9.43	10.85				
20.11.2025	74.85	17.35	13.37	14.95	45.27	12.65	9.47	10.34	73.1	26.85	11.13	13.44	65.76	15.27	8.43	13.63				
21.11.2025	54.46	22.83	12.06	13.23	54.65	17.4	7.27	8.55	59.17	22.31	9.01	10.8	55.52	19.8	8.71	11.68				
26.11.2025	58.67	13.64	11.04	12.38	50.26	12.11	7.91	9.22	61.17	19.14	8.48	12.66	61.48	17.58	8.22	11.49				
27.11.2025	69.61	19.93	10.26	12.73	46.66	17.5	7.38	10.5	58.56	15.46	7.66	9.82	55.01	16.33	9.21	10.56				
05.12.2025	62.68	22.47	9.7	11.21	63.41	22.37	9.31	11.59	58.07	22.42	7.44	9.12	48.83	14.16	6.51	8.46				
06.12.2025	55.52	17.52	7.34	9.36	48.79	18.59	6.07	8.22	73.67	30.75	11.49	13.81	60.2	23.45	10.22	12.55				
10.12.2025	63.21	28.37	10.02	13.24	59.7	24.55	9.17	12.51	61.23	17.62	9.51	11.54	65.2	28.6	12.23	14.81				
11.12.2025	57.44	19.82	8.26	10.25	52.28	19.38	7.59	9.4	56.2	23.85	7.42	9.16	47.15	19.51	6.75	9.52				
19.12.2025	45.76	21.33	6.59	8.57	39.62	14.66	5.74	8.94	70.35	27.49	13.35	15.1	63.08	22.31	9.46	11.47				
20.12.2025	63.22	26.28	10.43	12.38	57.32	20.58	8.31	10.36	63.73	24.19	10.78	12.25	48.15	17.67	8.48	12.76				
24.12.2025	52.79	18.24	11.16	14.02	61.8	25.89	10.49	13.42	69.15	31.69	11.84	14.63	66.43	28.61	10.82	13.42				
25.12.2025	64.5	23.1	10.37	12.03	44.87	14.67	8.16	10.45	54.18	19.18	8.33	10.45	61.37	21.26	9.69	11.06				
07.01.2026	65.67	18.97	9.65	11.63	61.82	21.59	9.25	11.36	62.76	23.44	9.52	9.12	53.92	21.52	6.48	8.28				
08.01.2026	58.22	17.56	7.3	9.17	50.88	17.92	6.03	8.05	72.59	29.94	11.43	13.52	57.43	22.45	10.16	12.3				
14.01.2026	65.47	23.4	7.77	12.97	57.71	19.0	9.12	12.25	63.4	17.45	11.32	11.3	67.48	15.1	12.16	14.51				
15.01.2026	59.06	20.28	8.22	10.04	55.89	15.37	9.73	9.21	58.93	23.33	7.38	8.97	49.62	17.23	6.71	9.33				
19.01.2026	48.0	20.12	9.91	8.40	53.91	14.78	5.71	8.75	74.02	24.76	13.27	16.21	65.41	19.13	11.25	11.24				
20.01.2026	61.91	25.89	10.36	12.12	48.71	19.44	8.26	10.15	60.61	25.16	11.95	12.0	51.18	17.33	12.47	12.5				
27.01.2026	50.31	17.16	9.42	13.74	64.45	14.92	10.42	13.14	73.01	23.28	11.77	14.33	69.26	19.13	10.76	13.14				
28.01.2026	66.96	22.42	8.62	14.64	40.14	13.3	9.64	10.24	51.15	18.57	9.64	10.24	58.22	18.76	12.0	11.67				
04.02.2026	69.59	17.91	7.47	8.54	51.03	17.78	7.0	8.7	79.44	20.97	7.11	8.2	61.43	17.08	7.37	9.45				
05.02.2026	69.6	24.46	10.21	10.78	60.72	15.01	8.53	8.74	65.71	24.63	9.36	10.6	70.66	14.52	9.24	9.76				

EC Half Yearly Compliance
Period: October 2025 to March 2026

DALMIA CEMENT (BHARAT) LIMITED

11.02.2026	63.68	22.99	9.72	12.03	53.96	16.89	6.75	7.44	78.54	20.12	8.62	10.88	68.52	16.76	8.99	10.82
12.02.2026	57.98	20.32	12.1	12.36	44.56	19.63	7.75	8.28	65.61	20.59	10.76	11.86	59.02	13.27	9.24	10.5
16.02.2026	72.26	19.32	13.1	14.47	47.79	14.36	9.28	10.01	70.53	23.73	10.9	13.01	64.71	16.23	8.26	13.19
17.02.2026	56.99	24.49	11.82	12.81	57.94	18.53	7.12	8.28	58.5	24.27	8.83	10.46	51.46	19.13	8.54	11.31
23.02.2026	60.53	16.11	10.82	11.98	51.54	14.7	7.75	8.92	63.03	19.7	8.31	12.25	57.93	15.43	8.06	11.12
24.02.2026	72.81	21.86	10.05	12.33	49.74	18.87	7.23	10.17	59.43	16.99	7.5	9.51	52.12	15.37	9.03	10.23
04.03.2026	54.69	12.45	12.34	13.54	52.97	16.59	8.67	8.64	49.11	21.18	9.26	9.93	46.36	18.57	7.93	9.89
05.03.2026	50.48	14.56	9.92	10.93	55.11	13.82	8.13	7.62	44.34	24.39	10.88	10.75	43.79	19.68	8.85	9.67
11.03.2026	48.28	15.85	13.71	13.8	46.44	18.01	9.4	8.82	48.18	16.24	8.53	9.71	42.84	18.96	10.26	10.72
12.03.2026	52.04	10.65	10.41	11.74	49.82	16.85	8.19	7.71	42.16	17.65	11.26	11.91	42.16	20.86	7.67	10.44
16.03.2026	41.44	13.57	9.55	10.72	43.98	16.96	6.77	8.23	44.41	18.96	10.13	10.86	44.79	17.35	9.8	9.85
17.03.2026	42.41	11.59	7.43	9.03	39.41	22.19	7.15	7.55	39.92	19.75	7.75	8.95	44.09	18.76	8.46	11.54
23.03.2026	45.02	11.62	11.87	12.52	41.35	15.87	6.31	8.09	40.36	18.58	8.87	9.45	41.41	21.89	7.71	11.24
24.03.2026	37.57	15.68	10.1	11.37	33.91	15.29	8.7	9.79	35.94	20.72	9.65	9.75	48.55	19.38	8.45	11.04
Average	56.95	18.22	10.31	12.19	49.67	15.87	8.10	9.56	59.57	20.51	9.78	11.43	55.02	17.43	9.14	11.46
NAAQS STD	100	60	80	80	100	60	80	80	100	60	80	80	100	60	80	80

Water Sprinkling System



Date/Time Long at 3:04:05 PM January 19, 2026
Trigger Source Geo: 0.500 mm/s, Mic: 130.0 dB(L)
Range Geo: 254.0 mm/s
Record Time 3.0 sec at 1024 sps
Operator/Setup: Operator/VINAYAK.mmb

Serial Number UM9188 V 10-90GC Micromate ISEE
Battery Level 3.7 Volts
Unit Calibration September 24, 2025 by UES New Delhi
File Name TEMP.EVT

Notes



Location: YADWAD AND KUNNAL LIMESTONE MINES
Client: M/S. DALMIA CEMENT (BHARAT) LIMITED
User Name: DCBL
General: Pit-2, N / NE / E / SE / S / SW / W / NW

Extended Notes

Microphone Linear Weighting
PSPL 113.3 dB(L) at 1.750 sec
ZC Freq 13 Hz
Channel Test Passed (Freq = 19.7 Hz Amp = 1180 mv)

	Tran	Vert	Long	
PPV	1.600	1.269	2.703	mm/s
PPV (Ponderated)	0.784	0.793	1.798	mm/s
PPV	134.1	132.1	138.6	dB
ZC Freq	73	57	57	Hz
Time (Rel. to Trig)	0.204	0.375	0.432	sec
Peak Acceleration	0.074	0.070	0.086	g
Peak Displacement	0.006	0.004	0.010	mm
Sensor Check	Passed	Passed	Passed	
Frequency	7.3	7.7	7.3	Hz
Overswing Ratio	3.6	3.4	3.5	

Peak Vector Sum 2.715 mm/s at 0.432 sec

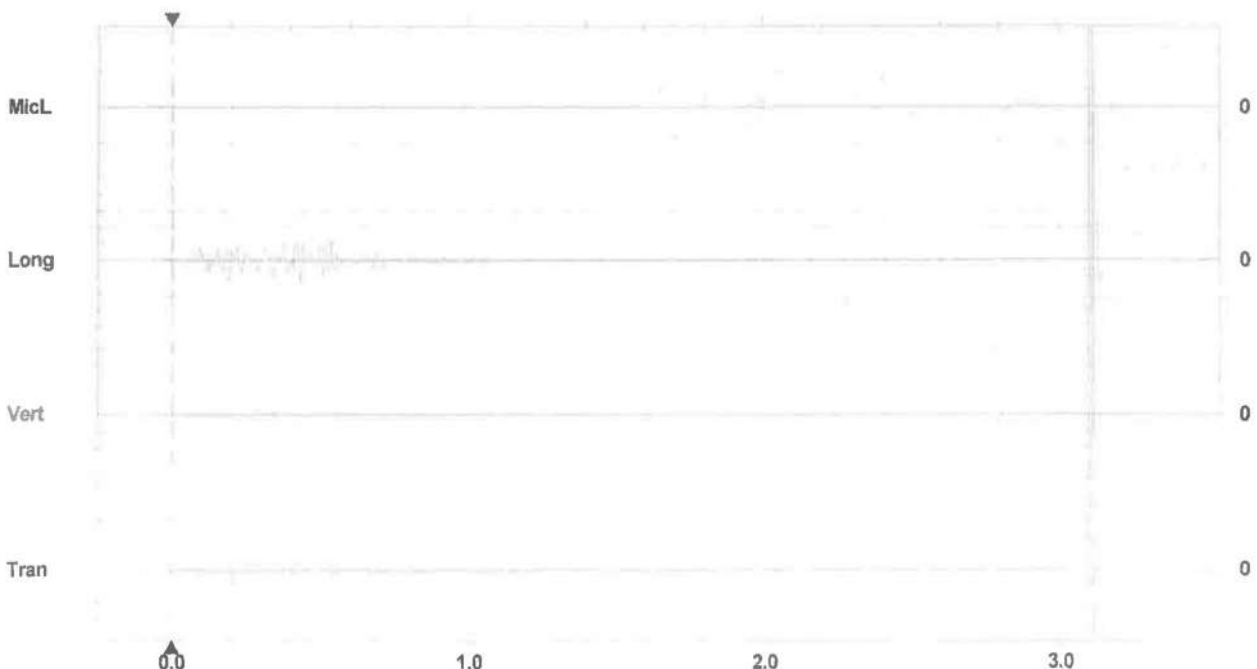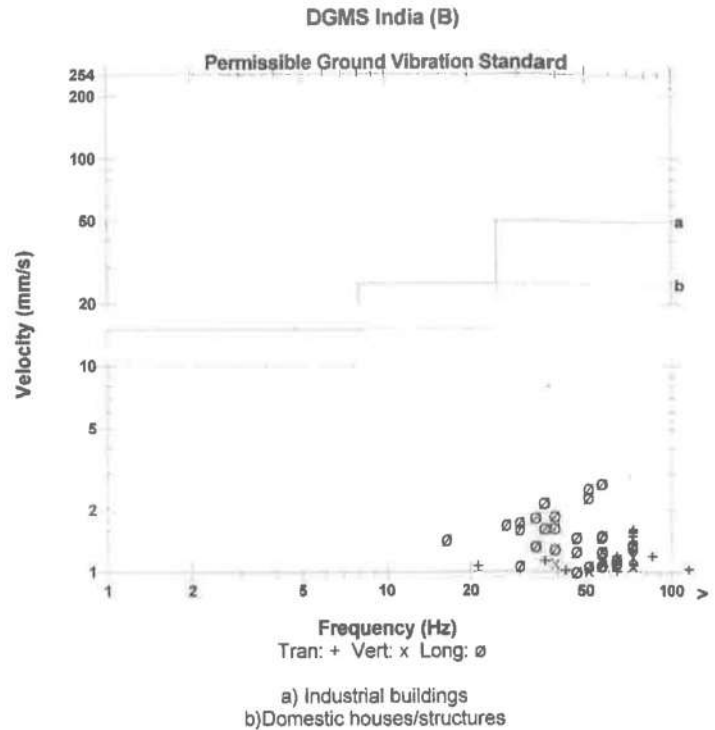

Time Scale: 0.20 sec/div **Amplitude Scale:** Geo: 2.000 mm/s/div Mic: 5.000 pa.(L)/div
Trigger = ▶

Sensor Check

Printed: January 28, 2026 (V 10.72 - 10.72)

Format © 1995-2014 Xmark Corporation



Blasting Vibration Event Report

Date/Time Long at 2:06:06 PM January 6, 2026
Trigger Source Geo: 0.500 mm/s, Mic: 130.0 dB(L)
Range Geo: 254.0 mm/s
Record Time 3.0 sec at 1024 sps
Operator/Setup: Operator/VINAYAK.mmb

Serial Number UM9188 V 10-90GC Micromate ISEE
Battery Level 3.7 Volts
Unit Calibration September 24, 2025 by UES New Delhi
File Name _TEMP.EVT

Notes



Location: YADWAD AND KUNNAL LIMESTONE MINES
Client: M/S. DALMIA CEMENT (BHARAT) LIMITED
User Name: DCBL
General: Pit-2, N / NE / E / SE / S / SW / W / NW

Extended Notes

Microphone Linear Weighting
PSPL 125.2 dB(L) at 1.763 sec
ZC Freq 23 Hz
Channel Test Passed (Freq = 19.7 Hz Amp = 1294 mv)

	Tran	Vert	Long	
PPV	0.575	0.662	0.552	mm/s
PPV (Ponderated)	0.271	0.277	0.365	mm/s
PPV	125.2	126.4	124.8	dB
ZC Freq	>100	>100	39	Hz
Time (Rel. to Trig)	0.129	0.226	0.000	sec
Peak Acceleration	0.035	0.043	0.032	g
Peak Displacement	0.002	0.002	0.002	mm
Sensor Check	Passed	Passed	Passed	
Frequency	7.3	7.7	7.3	Hz
Overswing Ratio	3.6	3.4	3.4	

Peak Vector Sum 0.747 mm/s at 0.238 sec

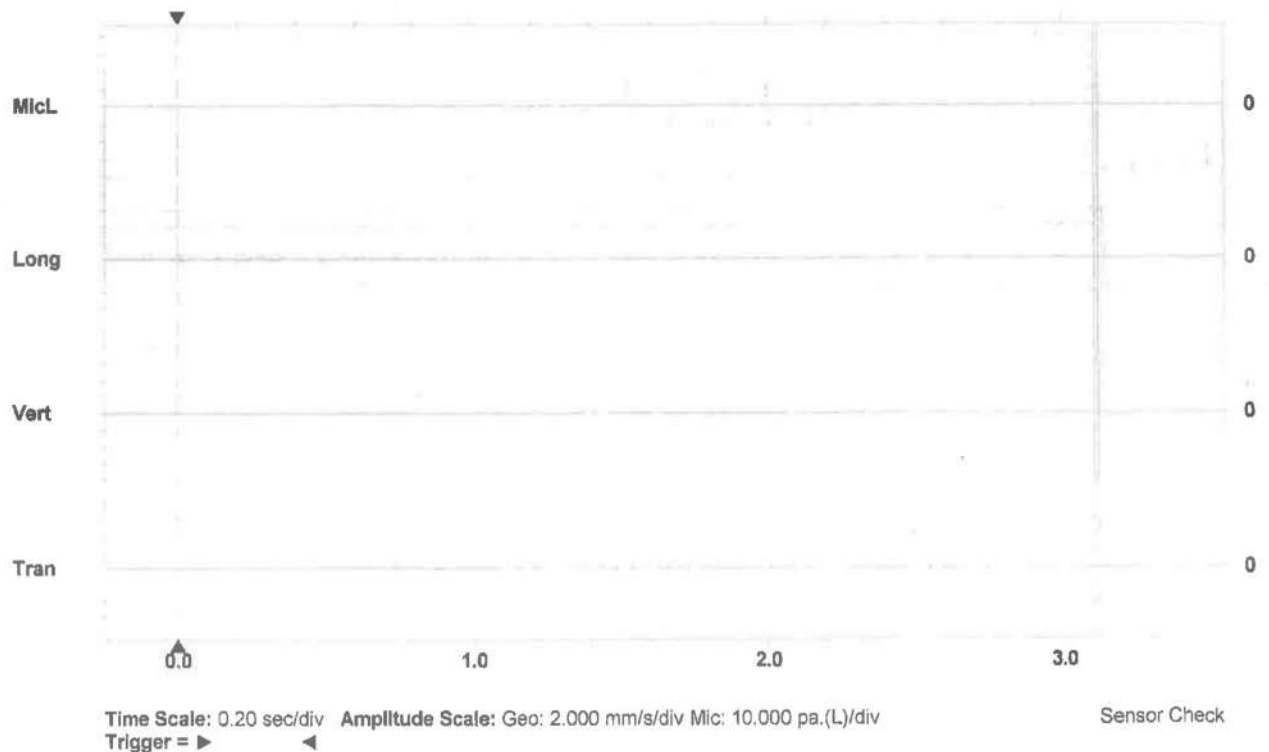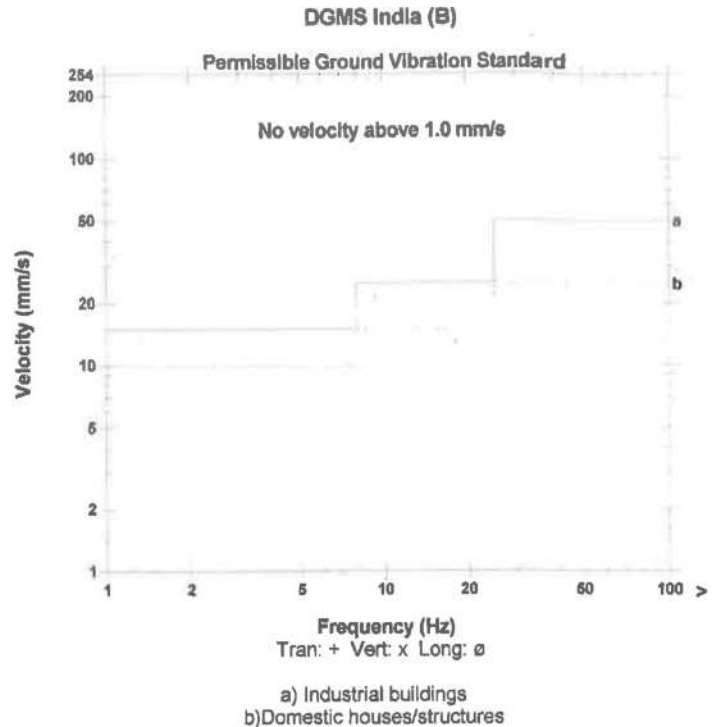

Printed: January 17, 2026 (V 10.72 - 10.72)

Format © 1995-2014 Xmark Corporation



Blasting Vibration Event Report

Date/Time Vert at 2:48:20 PM January 20, 2026
Trigger Source Geo: 0.500 mm/s, Mic: 130.0 dB(L)
Range Geo: 254.0 mm/s
Record Time 3.0 sec at 1024 sps
Operator/Setup: Operator/VINAYAK.mmb

Serial Number UM9188 V 10-90GC Micromate ISEE
Battery Level 3.7 Volts
Unit Calibration September 24, 2025 by UES New Delhi
File Name TEMP.EVT

Notes



Location: YADWAD AND KUNNAL LIMESTONE MINES
Client: M/S. DALMIA CEMENT (BHARAT) LIMITED
User Name: DCBL
General: Pit-2, N / NE / E / SE / S / SW / W / NW

Extended Notes

Microphone Linear Weighting
PSPL 116.9 dB(L) at 1.355 sec
ZC Freq 13 Hz
Channel Test Passed (Freq = 19.7 Hz Amp = 1195 mv)

	Tran	Vert	Long	
PPV	1.135	1.758	0.851	mm/s
PPV (Ponderated)	0.762	1.198	0.571	mm/s
PPV	131.1	134.9	128.6	dB
ZC Freq	32	32	51	Hz
Time (Rel. to Trig)	0.273	0.253	0.229	sec
Peak Acceleration	0.035	0.063	0.036	g
Peak Displacement	0.004	0.007	0.003	mm
Sensor Check	Passed	Passed	Passed	
Frequency	7.3	7.7	7.3	Hz
Overswing Ratio	3.6	3.4	3.4	

Peak Vector Sum 1.771 mm/s at 0.253 sec

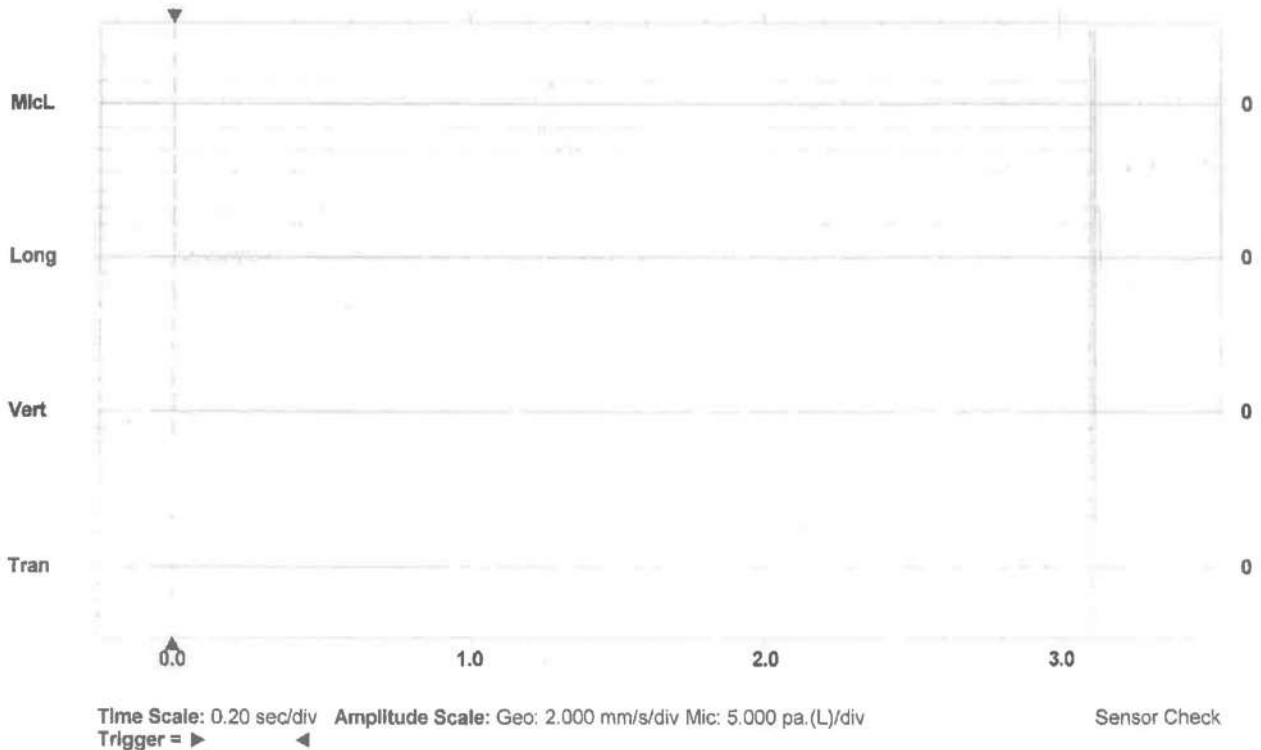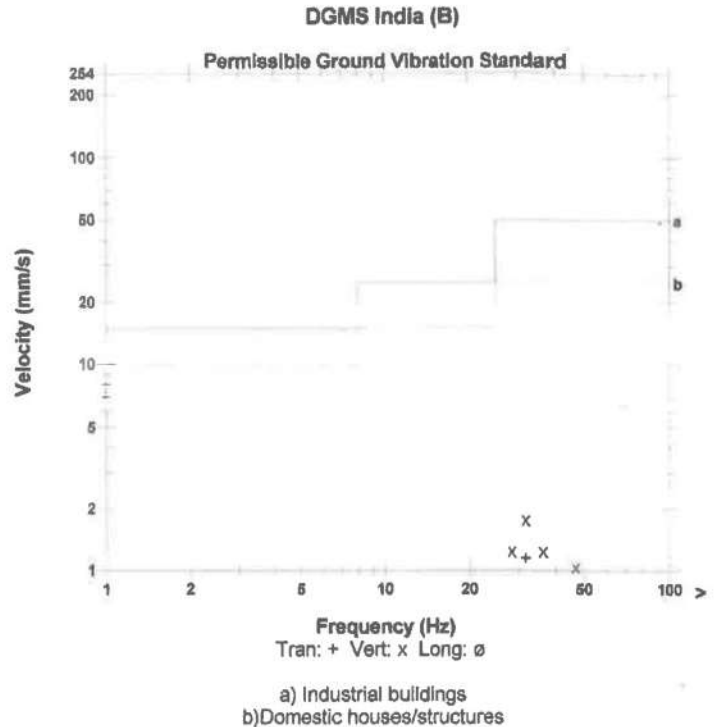

Printed: January 28, 2026 (V 10.72 - 10.72)

Format © 1995-2014 Xmark Corporation



Serial Number UM9188 V 10-90GC Micromate ISEE
Battery Level 3.7 Volts
Unit Calibration September 24, 2025 by UES New Delhi
File Name TEMP.EVT

DGMS India (B)

Permissible Ground Vibration Standard

Figure 1 is a log-log plot titled "Permissible Ground Vibration Standard". The y-axis is labeled "Velocity (mm/s)" and ranges from 1 to 254 on a logarithmic scale. The x-axis is labeled "Time (s)" and ranges from 1 to 100 on a logarithmic scale. The plot shows a step function representing the permissible standard: 15 mm/s from 1 to 8 seconds, 25 mm/s from 8 to 25 seconds, and 50 mm/s from 25 to 100 seconds. Two data series are plotted: 'a' (circles) and 'b' (crosses). Series 'a' follows the standard closely, while series 'b' shows significantly lower velocities, mostly below 2 mm/s.

Frequency (Hz)
 Tran: + Vert: x Long: ø

a) Industrial buildings
 b) Domestic houses/structures

	Tran	Vert	Long	
PPV	1.766	0.883	1.084	mm/s
PPV (Ponderated)	1.262	0.575	0.744	mm/s
PPV	134.9	128.9	130.5	
ZC Freq	43	37	32	Hz
Time (Rel. to Trlg)	0.220	0.170	0.309	sec
Peak Acceleration	0.058	0.031	0.037	g
Peak Displacement	0.006	0.003	0.005	mm
Sensor Check	Passed	Passed	Passed	
Frequency	7.3	7.7	7.5	Hz
Overswing Ratio	3.6	3.4	3.3	

Peak Vector Sum 1.841 mm/s at 0.219 sec

Time Scale: 0.20 sec/div Amplitude Scale: Geo: 2.000 mm/s/div Mic: 5 000 pa.(L)/div
Trigger = ▶ ◀

Sensor Check

Printed: December 18, 2025 (V 10.72 - 10.72)

Format © 1995-2014 Xmark Corporation



Blasting Vibration Event Report

Date/Time Vert at 3:01:47 PM December 26, 2025
Trigger Source Geo: 0.500 mm/s, Mic: 130.0 dB(L)
Range Geo: 254.0 mm/s
Record Time 3.0 sec at 1024 sps
Operator/Setup: Operator/VINAYAK.mmb

Serial Number UM9188 V 10-90GC Micromate ISEE
Battery Level 3.7 Volts
Unit Calibration September 24, 2025 by UES New Delhi
File Name _TEMP.EVT

Notes



Location: YADWAD AND KUNNAL LIMESTONE MINES
Client: M/S. DALMIA CEMENT (BHARAT) LIMITED
User Name: DCBL
General: Pit-2, N / NE / E / SE / S / SW / W / NW

Extended Notes

Microphone Linear Weighting
PSPL 113.6 dB(L) at 1.648 sec
ZC Freq 22 Hz
Channel Test Passed (Freq = 19.7 Hz Amp = 1272 mv)

	Tran	Vert	Long	
PPV	0.962	1.103	0.859	mm/s
PPV (Ponderated)	0.449	0.661	0.357	mm/s
PPV	129.7	130.9	128.7	dB
ZC Freq	37	73	>100	Hz
Time (Rel. to Trig)	0.165	0.180	0.153	sec
Peak Acceleration	0.053	0.071	0.062	g
Peak Displacement	0.004	0.003	0.002	mm
Sensor Check	Passed	Passed	Passed	
Frequency	7.3	7.7	7.5	Hz
Overswing Ratio	3.6	3.4	3.3	

Peak Vector Sum 1.210 mm/s at 0.180 sec

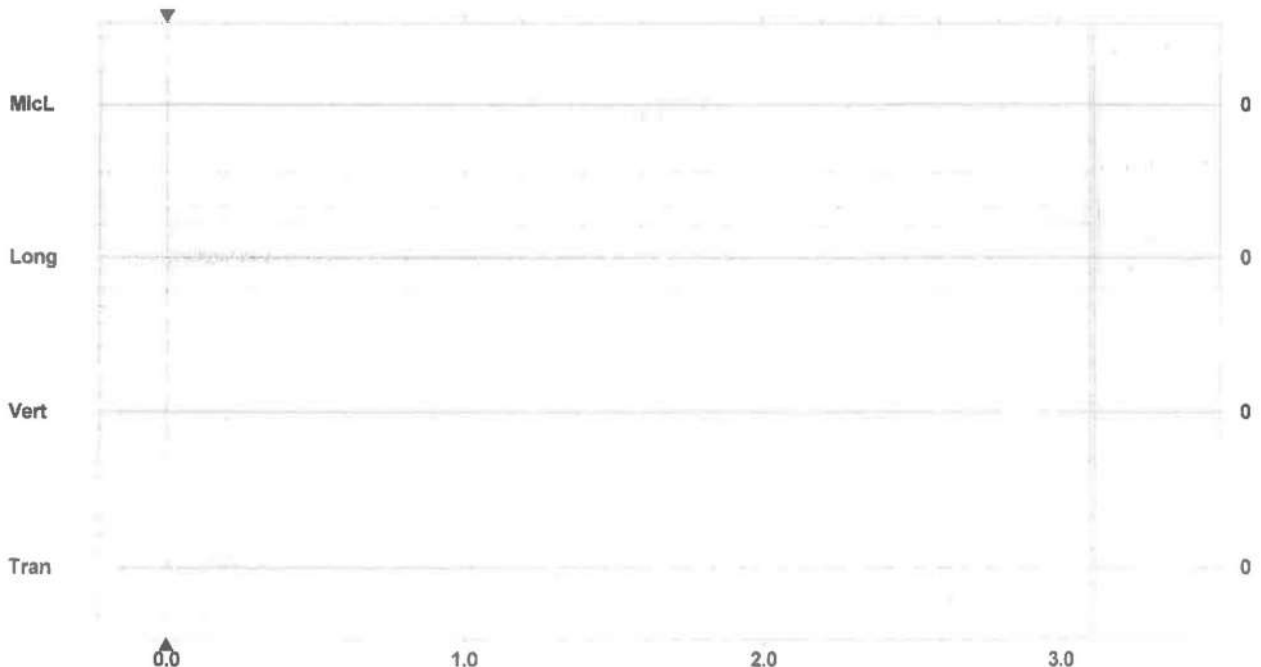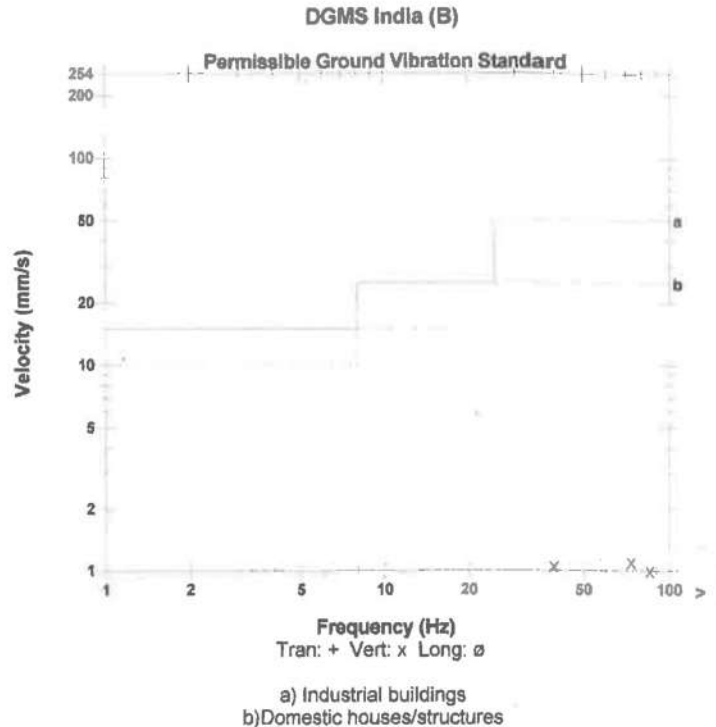

Time Scale: 0.20 sec/div Amplitude Scale: Geo: 2.000 mm/s/div Mic: 5.000 pa.(L)/div
Trigger = ▶ ◀

Sensor Check

Printed: January 17, 2026 (V 10.72 - 10.72)

Format © 1995-2014 Xmark Corporation



Blasting Vibration Event Report

Date/Time Long at 3:04:16 PM February 20, 2026
Trigger Source Geo: 0.500 mm/s, Mic: 130.0 dB(L)
Range Geo: 254.0 mm/s
Record Time 3.0 sec at 1024 sps
Operator/Setup: Operator/VINAYAK.mmb

Serial Number UM9188 V 10-90GC Micromate ISEE
Battery Level 3.5 Volts
Unit Calibration September 24, 2025 by UES New Delhi
File Name _TEMP.EVT

Notes



Location: YADWAD AND KUNNAL LIMESTONE MINES
Client: M/S. DALMIA CEMENT (BHARAT) LIMITED
User Name: DCBL
General: Pit-2, N / NE / E / SE / S / SW / W / NW

Extended Notes

Microphone Linear Weighting
PSPL 108.3 dB(L) at 2.391 sec
ZC Freq 20 Hz
Channel Test Passed (Freq = 19.7 Hz Amp = 1027 mv)

	Tran	Vert	Long	
PPV	1.127	1.088	1.844	mm/s
PPV (Ponderated)	0.761	0.952	1.192	mm/s
PPV	131.0	130.7	135.3	dB
ZC Freq	43	24	47	Hz
Time (Rel. to Trig)	0.384	0.492	0.224	sec
Peak Acceleration	0.080	0.065	0.071	g
Peak Displacement	0.007	0.007	0.009	mm
Sensor Check	Passed	Passed	Passed	
Frequency	7.5	7.7	7.3	Hz
Overswing Ratio	3.5	3.4	3.4	

Peak Vector Sum 2.016 mm/s at 0.225 sec

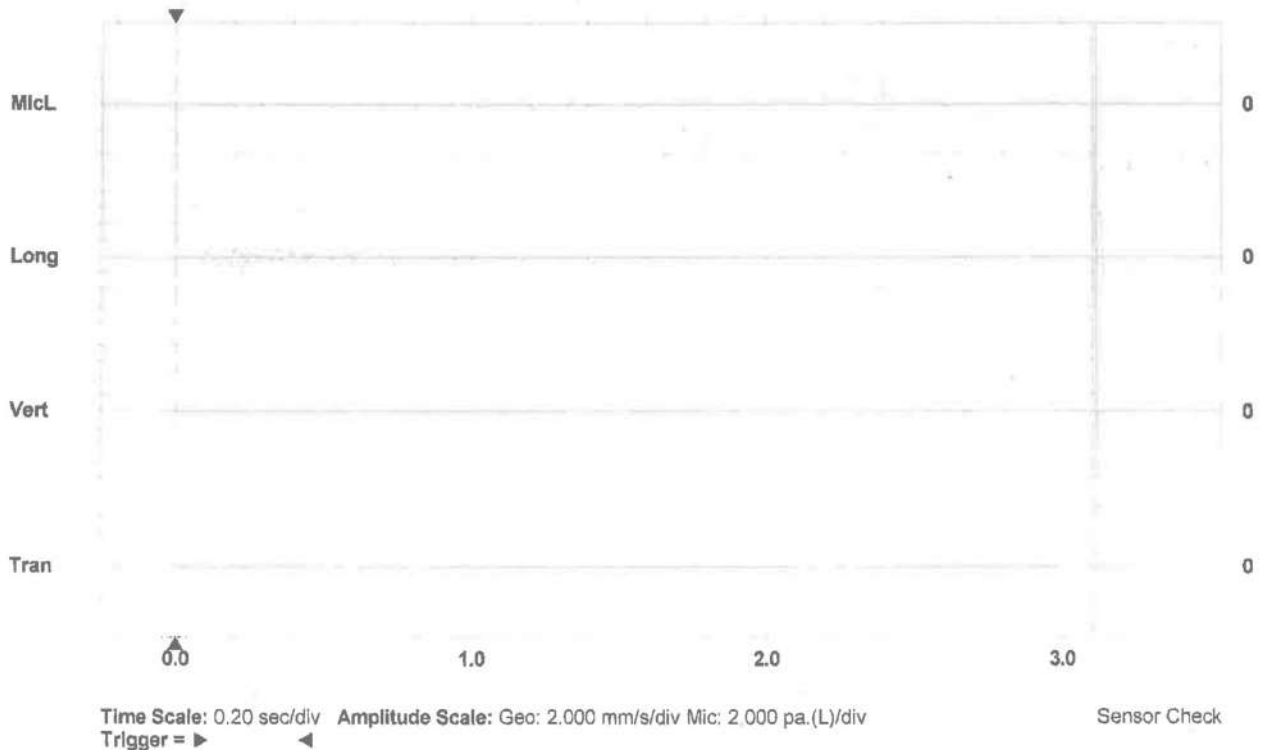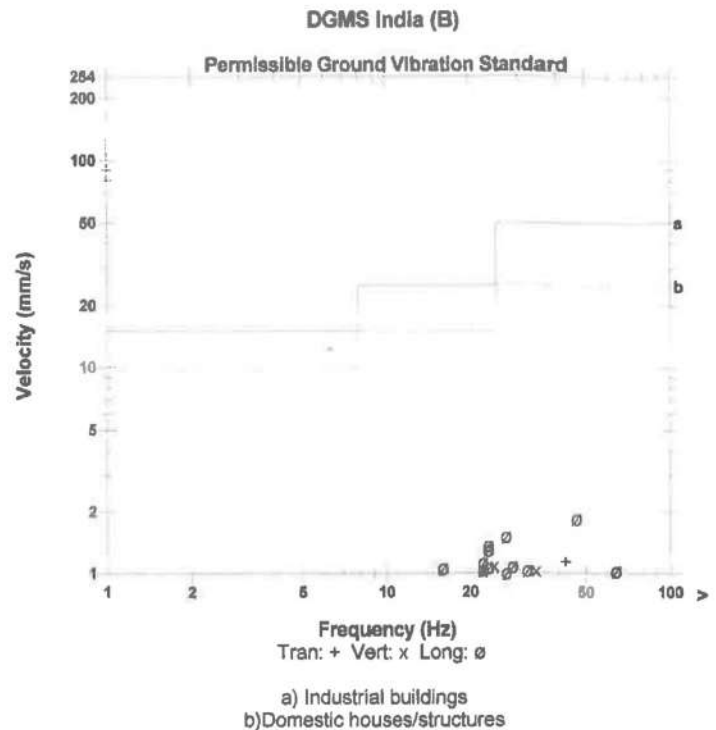

Printed: February 28, 2026 (V 10.72 - 10.72)

Format © 1995-2014 Xmark Corporation

Catch Drains



Rain Water Harvesting system



Mansarovar RWH Pond at Plant



Pushkar RWH Pond at Plant



Rain water harvesting reservoir of YKLM



Rain water harvesting Mining pit of YKLM



Storm water drainage system



DALMIA CEMENT (BHARAT) LIMITED

EC Half Yearly Compliance
Period: October 2025 to March 2026

RESPIRABLE DUST SAMPLING

Sr. No	Locations	Nov-25			Mar-26		
		Date of sampling	Personal Dust Concentration in µg/cum	Free Silica Content %	Date of sampling	Personal Dust Concentration in µg/cum	Free Silica Content %
1	Inside HEME Cabin	04.11.2025	0.140	ND	04.02.2026	0.132	ND
2	Near Packer - Packing Plant	08.11.2025	0.527	ND	07.02.2026	1.139	ND
3	Inside CCR DCBL	07.11.2025	0.037	ND	07.02.2026	0.036	ND
4	Cement Mill CCR	05.11.2025	0.122	ND	05.02.2026	1.327	ND
5	Inside CCR-CPP	06.11.2025	0.031	ND	06.02.2026	0.083	ND
							<1%
							<1%
							<1%
							<1%
							<1%

FUGITIVE EMISSION MONITORING mg/m3, (MINES)

Sl No.	Name of the Station	Oct-25	Nov-25	Dec-25	Jan-26	Feb-26	Mar-26
1	Near Mines office	0.14	0.11	0.13	0.12	0.19	0.19
2	Near Lime stone crusher	0.28	0.38	0.34	0.31	0.52	0.34
3	Near Loading Site- Mines	0.34	0.31	0.27	0.25	0.39	0.29
4	Near Haulage Road	0.37	0.34	0.37	0.36	0.38	0.32
5	Near LS crusher -Mines	0.22	0.26	0.29	0.25	0.31	0.22

Plantation Report

S.N	Unit	2016-17	2017-18	2018-19	2019-20	2020-21	2021-22	2022-23	2023-24	2024-25	2025-26	Total Plantation
1	No. of Trees Planted	230	4484	8066	1884	2500	2800	2900	1700	4635	7500	36699
2	Area Covered (Ha)	0.85	16.04	22.07	0.75	2	2.5	2.5	0.65	3	5	55.36
3	Survival Rate (%)	91.00	93.00	93.00	95.00	95.00	95.00	81.30	82.00	85.00	85.00	89.53







Latitude: 16.199793
Longitude: 75.211613
Elevation: 606.06±42.3 m
Accuracy: 1.6 m
Time: 11-08-2025 10:27
Note: Dalmia Cement Bharat Ltd, Belgaum
STP Plant

VEHICLE WASH TREATED WATER QUALITY									
Sl No	Parameters	Unit	Oct-25	Nov-25	Dec-25	Jan-26	Feb-26	Mar-26	As per GSR 422 (E)
1	pH	-	8.34	8.06	8.2	8.1	8.11	7.9	5.50 to 9.0
2	Total Dissolved Solids	mg/l	1340	948	972	965	890	918	-
3	Total Suspended Solids	mg/L	22.0	28.0	26	25	31.0	21.4	100
4	Biochemical Oxygen Demand for 3 days at 27°C	mg/L	8.0	12.0	14	14.0	10.4	12.8	30
5	Chemical Oxygen Demand as O ₂	mg/L	53.04	65.28	68.39	71.39	72.41	77.96	250
6	Oil & Grease	mg/L	2.0	4.0	3.8	2.4	5.3	2.9	10
7	Nickel as Ni	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	3.0
8	Copper as Cu	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	3.0
9	Zinc as Zn	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	5.0
10	Lead as Pb	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	0.10
11	Colour	Hazen units	<5.0	<5.0	<5.0	<5.0	<5.0	<5.0	-
12	Ambient Temperature	°C	25.2	25.2	25.2	25.8	25.2	26.8	-
13	Odour	-	Disagreeable	Disagreeable	Disagreeable	Disagreeable	Disagreeable	Disagreeable	-
14	Total Residual chlorine	mg/l	0.00	0.00	0.00	0.00	0.00	0	1
15	Ammonia as NH ₃	mg/L	1.12	2.24	1.12	2.63	1.83	2.17	5.0
16	Kjeldahl nitrogen as NH ₃	mg/L	8.16	8.56	8.16	8.19	7.88	8.83	100
17	Ammonical nitrogen as N	mg/L	5.6	11.76	10.52	9.62	17.1	10.86	50
18	Cadmium as Cd	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	2.00
19	Mercury as Hg	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	0.01
20	Arsenic as As	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	-
21	Selenium As Se	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	0.05
22	Boron as B	mg/L	BDL	BDL	BDL	BDL	BDL	BDL	-
23	Percent Sodium	mg/L	3.14	2.74	3.14	2.12	3.41	2.02	-

